MARINE FORCES PACIFIC G-4

MPSRON-2 MMC-8 Sourcing OPT
Maj Escarcega
G-4 Mobility Surface Officer

Purpose

- Provide SA to attendees on initial HQMC proposals for MPSRON-2 MMC-8
- Develop RFI’s to clarify HQMC intent and sourcing situation

MMC-8 Adjustments

- **Purpose: To revise HQMC MMC-8 planning guidance in reaction to present operational situation**
- **Endstate: Revised, coordinated PO/LP guidance for MMC-8**
- **Issue:**
  - **MPSRON-2 Attainment**
    - **Equipment still supporting OIF**
    - **SGEWG will source some assets from MPF attainment**
    - **CMC Guidance for MMC-8 ≥ 98% (CMC 152300Z Nov 03)**
    - **Current Class VII attainment projection for MPSRON-2:**

	Phillips	Kocak	Lopez	Button	Stockham
Class VII	73%	59%	35%	18%	10%
MCGERR	73%	59%	35%	30%	26%
Sustainment					

*Numbers in chart reflect attainment forecast assuming execution of current SGEWG

COAs

- **COA 1: “Steady State”**
  - **Reconstitute MPSRON-2 with lower than normal Class VII attainment**
  - **MPSRON-2 reconstituted after MPSRON-1**
  - **Reconstitute two MPSRON-3 MPS’s during FY05**
- **COA 2: “Swap”**
  - **Induct MPS-3 after MPS-1**
  - **Re-evaluate ability to reconstitute MPS-2 in FY 06**

COA 1 – "Steady State"

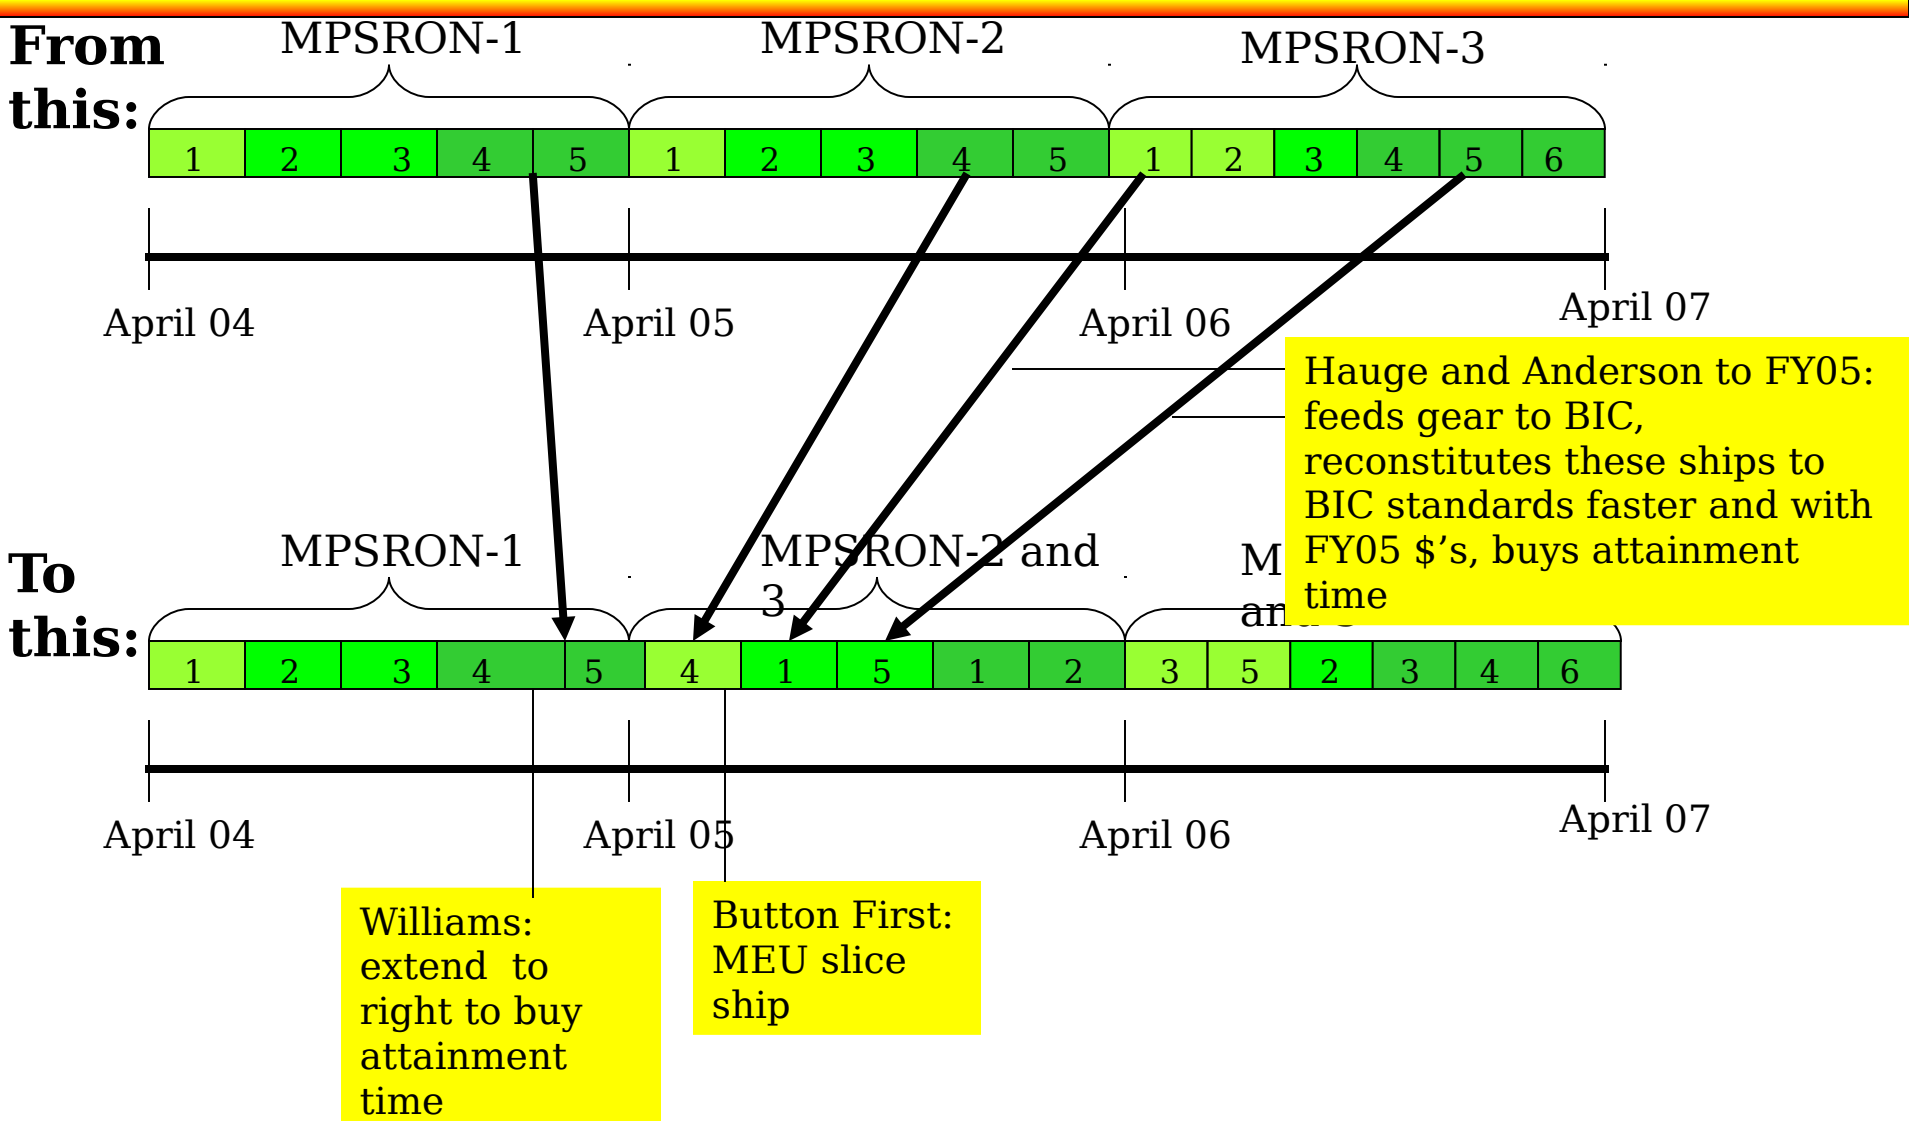
From this:
MPSRON-1
MPSRON-2
MPSRON-3
1 2 3 4 5 1 2 3 4 5 1 2 3 4 5 6
April 04
April 05
April 06
April 07
Hauge and Anderson to FY05: feeds gear to BIC, reconstitutes these ships to BIC standards faster and with FY05 $'s, buys attainment time
To this:
MPSRON-1
MPSRON-2 and 3
1 2 3 4 5 4 1 5 1 2 3 5 2 3 4 6
April 04
April 05
April 06
April 07
Williams: extend to right to buy attainment time
Button First: MEU slice ship

COA 1 – "Steady State"

- **COA 1: "Steady State"**
  - **Reconstitute MPSRON-2 after MPSRON-1**
  - **Reconstitute two MPSRON-3 MPS's during FY05**
    - **Accept reduced Class VII attainment levels**
    - **Maintain mirror-imaging capability/concept to the greatest extent possible**
    - **Priority of effort goes to designated Swing-Ships**
    - **Induct (2) MPS-3 (Reconstituted) MPS during FY05**
    - **Adjust MMC-8 schedule to maximize MPS-2 capabilities with available attainment.**

COA 1 PROs

- **Flexibility focused on Operational Requirements**
  - MPS-2 provides swing-ships when MPS-3 begins MMC-8
  - Support provided to Combatant Commanders: most prepo capability available soonest
  - Shows USMC commitment to reconstitution of strategic prepo assets
  - Attainment normal except for Class VII
- **Gains MPSRON-2 attainment time at low risk**
  - Potential for leveling of LOGCOM SOW regardless of operational uncertainty
  - Honeywell is a long term operational enabler that should be protected
- **Induct Two MPSRON-3 MPS's into MMC in FY05**
  - Hauge/Anderson reconstituted in Kuwait – more time for repairs
  - Utilize FY05 Supplemental Funds
- **Extending ROS status saves some operating cost**

COA-1 CONs

- **May extend overall time required to reconstitute MPSRON-2**
  - Potentially still at less than normal Class VII attainment
- **Hull cert and ship flow adjustments required during MMC-9**
- **Must Educate the COCOM that MPS-2 Class VII attainment is lower than normal.**

COA 2 – “Swap”

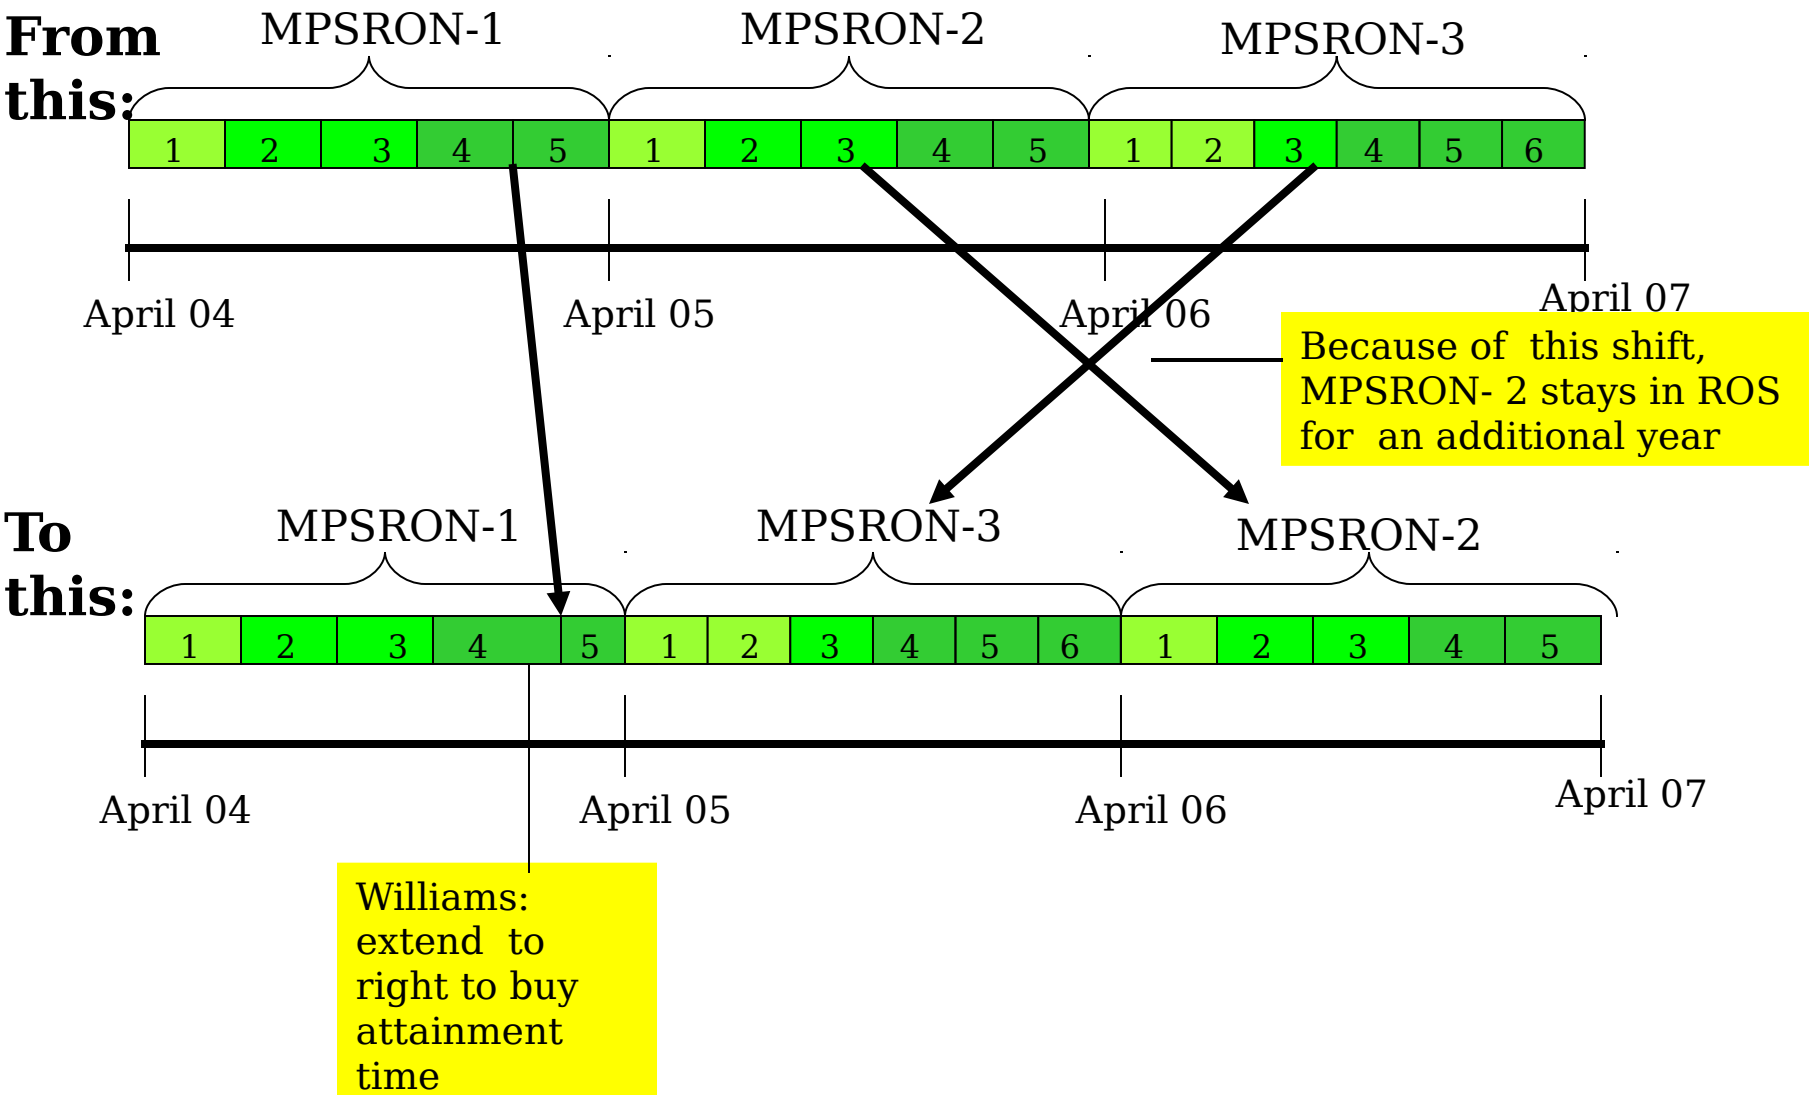
From this:
MPSRON-1
MPSRON-2
MPSRON-3
1 2 3 4 5 1 2 3 4 5 1 2 3 4 5 6
April 04
April 05
April 06
April 07
Because of this shift, MPSRON- 2 stays in ROS for an additional year
To this:
MPSRON-1
MPSRON-3
MPSRON-2
1 2 3 4 5 1 2 3 4 5 6 1 2 3 4 5
April 04
April 05
April 06
April 07
Williams: extend to right to buy attainment time

COA 2 – “Swap”

- **COA 2: Induct MPS-3 after MPS-1**
  - **Swap MPS-3 with MPS-2**
  - **Adjust MMC-8 schedule as required.**
  - **Re-evaluate ability to reconstitute MPS-2 in FY 06**

COA-2 PROs

- Allows maximum attainment time for MPS-2
- Saves money by keeping MPS-2 in ROS longer
- Executes FY05 supplemental funding request

COA-2 CONs

- **MPSRON-2 reconstitution delayed**
  - May be at no better attainment
  - Forces decision with less options available
    - Must reconstitute MPSRON-2 under prevailing circumstances at that time or bring MPSRON-1 in one year early
- **May present other out-year funding challenges**
- **Negates ability to Prepo sustainment stocks, EAF, NMCB, and NFH**
- **Missed opportunity to Prepo swing-ships**
  - Only MPS-1 swing-ship available during MPS-3 MMC sked

COA 3 – "Steady/Swap"

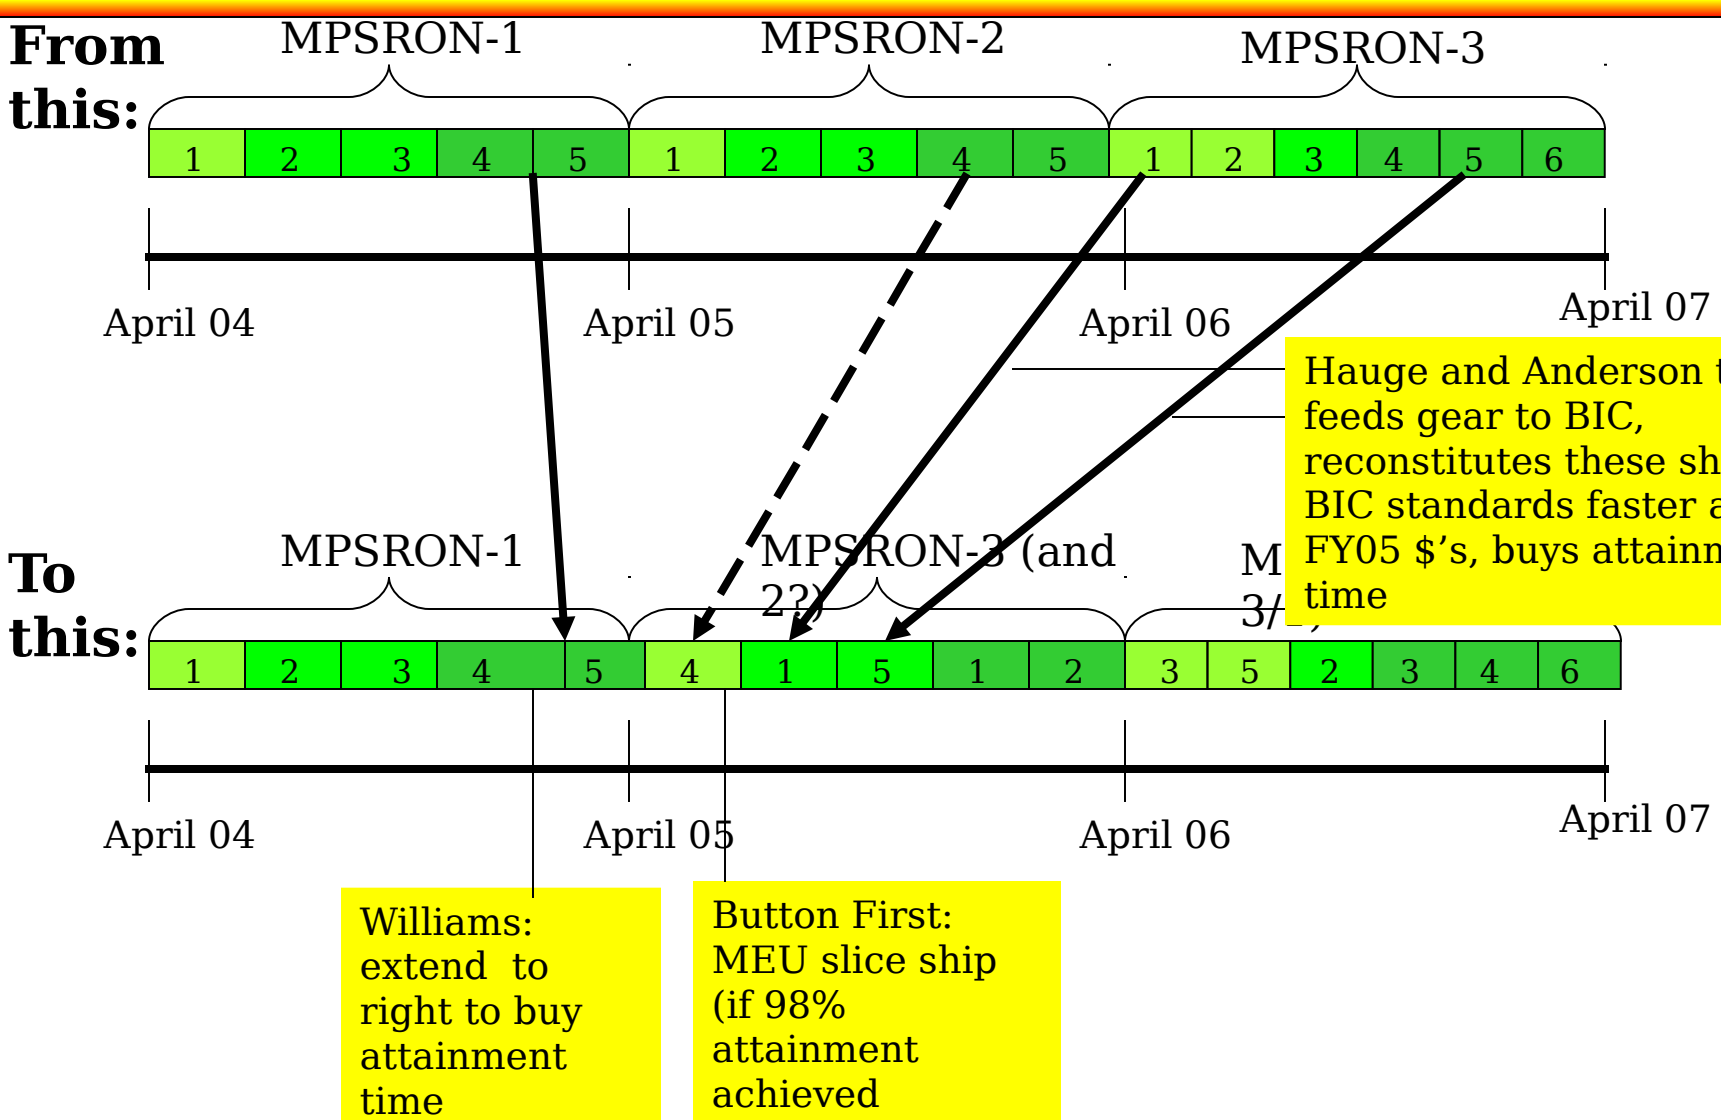
From this:
MPSRON-1
MPSRON-2
MPSRON-3
1 2 3 4 5 1 2 3 4 5 1 2 3 4 5 6
April 04
April 05
April 06
April 07
Hauge and Anderson to FY05: feeds gear to BIC, reconstitutes these ships to BIC standards faster and with FY05 $'s, buys attainment time
To this:
MPSRON-1
MPSRON-3 (and 2?)
1 2 3 4 5 4 1 5 1 2 3 5 2 3 4 6
April 04
April 05
April 06
April 07
Williams: extend to right to buy attainment time
Button First: MEU slice ship (if 98% attainment achieved

COA-3 Steady/Swap

- **Swap MPSRON-2 with MPSRON-3 schedule**
- **Shuffle Ships in MPSRON-3**
  - **Worst first – Pull in Hauge and Anderson first**
- **Substitute MPSRON-2 ships for MPSRON-3 ships when 98% attainment can be achieved per original CMC guidance for MMC-8 (CMC 152300Z Nov 03)**
- **Priority is on swing-ships only if 98% attainment achieved**
- **MPSRON-1 ships may end coming in early if MPSRON-2 ships can't achieve 98% attainment and all of MPSRON-3 completes MMC-8**

COA-3 Pros

- **Best supports PACOM “O” plans by improving MPSRON-3 sooner**
  - **MPSRON-2 ships alternate oplift**
- **Extends time to source shortfalls ISO MPSRON-2**
  - **Let’s you address concerns with equipment sourcing for higher priorities**
- **Maintains the workforce**
- **Lower attainment is not accepted as this only produces floating warehouses vice capabilities**

COA-3 Cons

- **No swing ship capability from MPSRON-2 unless 98% attainment can be achieved**
- **Schedule for ships, RAC Team, and BIC must remain flexible as sourcing efforts determine when to substitute a MPSRON-2 ship for a MPSRON-3 ship and push back/reschedule all other ships.**

Recommendation

- ❑ **COA-1: Reconstitute MPSRON-2 at a lower than normal Class VII attainment level and reconstitute two MPSRON-3 ships in FY05**

- ❑ **COA-2: Swap MPS-3 w/MPS-2 and re-evaluate the ability to Reconstitute MPS-2 in FY06.**

✓

- ❑ **Other**

RFI’s: Details required for thorough operational assessement

- Clarify on where the projected attainment for MPSRON-2 is coming from: LOGCOM in stores rework, MPF, EAP, acquisitions
  - How is Opfor affected?
- Need breakdown of the shortages
- What extent executing either of the COA's will improve the attainment with the additional time BICMD will gain for attainment
- Priorities for sourcing: Base/Stations, MPF, Unit T/E’s, OIF etc…
